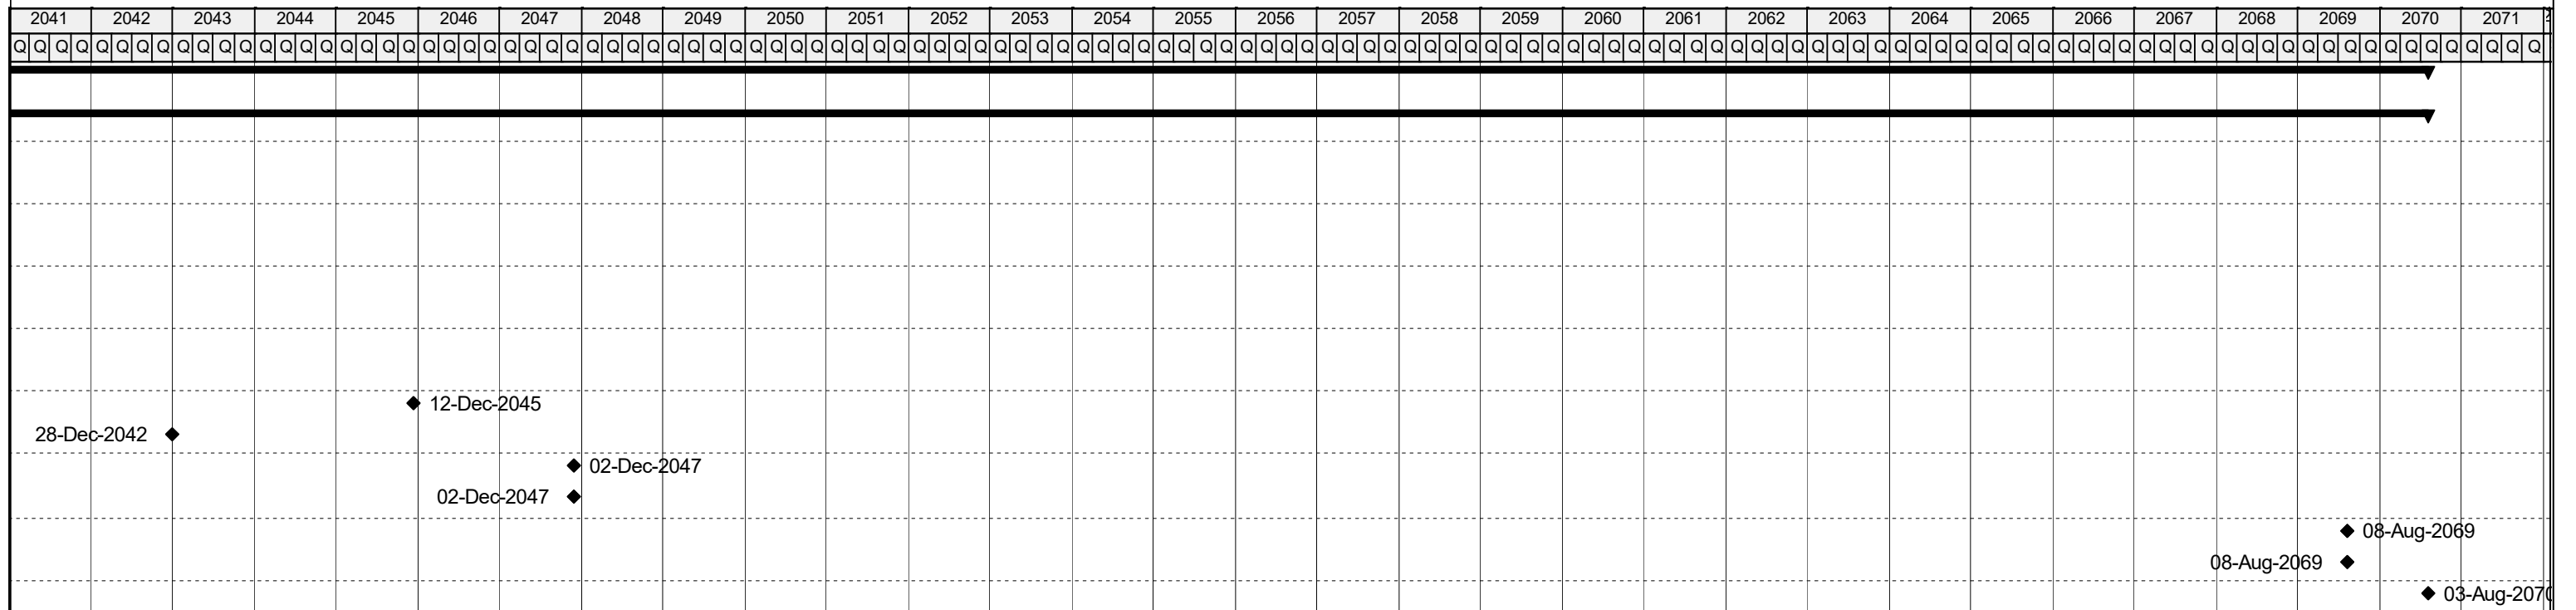






Activity ID	Activity Name	Duration	Start	Finish	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037	2038	2039	2040	2041	2042
					Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Blackwater Gold Project		48.0y	31-Mar-2023	03-Aug-2070	▶																				
1 - Major Milestones		48.0y	31-Mar-2023	03-Aug-2070	▶																				
2 - Construction Schedule		2.5y	31-Mar-2023	01-Oct-2025	▶																				
3 - Year +1 to Year +5		5.6y	02-Sep-2024	06-Mar-2030	▶																				
4 - Year +6 to Year +10		5.0y	06-Mar-2030	08-Feb-2035	▶																				
5 - Year +11 to Year +18		11.0y	08-Feb-2035	12-Dec-2045	▶																				
6 - Year +19 to Year +23		5.0y	28-Dec-2042	02-Dec-2047	▶																				
7 - Year +24 to Year +45		22.0y	02-Dec-2047	08-Aug-2069	▶																				
8 - Post Closure Year +46		1.0y	08-Aug-2069	03-Aug-2070	▶																				

Activity Duration
 Activity Duration
 summary

TASK filter: All Activities






























Date	Revision	Checked	Approved
17-Jan-2025	V.7: Prepared pursuant to: Blackwater Decision Statement condition 11.2	BW	JNL / RT



 Activity Duration  summary
 Activity Duration
 Milestone

TASK filter: WBS .

Date	Revision	Checked	Approved
17-Jan-2025	V.7: Prepared pursuant to:	BW	JNL / RT
	Blackwater Decision Statement condition 11.2		



Activity ID	Activity Name	Duration	Start	Finish	2023												2024												2025												026	
					N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	O		N
Blackwater Gold Project																																										
2 - Construction Schedule																																										
Open Pit																																										
A1120	Vegetation clearing, grubbing and surface preparation of initial pit phases	1.4y	31-Mar-2023	23-Aug-2024	31-Mar-2023																																					
A1140	Commissioning of initial mine fleet and addition to in-pit mine fleet	1.1y	18-Aug-2023	05-Oct-2024																																						
A1150	Starter Pit – Pre-Strip and Mining to 1,610 metres above sea level (masl) bench	0.4y	05-Oct-2024	22-Feb-2025																																						
A1160	Construction Borrow Pit – Mining to 1,510 masl bench	0.3y	14-Nov-2024	14-Mar-2025																																						
Process Plant																																										
A1170	Foundation construction ROM	1.4y	01-Aug-2023	31-Dec-2024																																						
A1180	Construction of facilities to pre-commissioning	1.6y	31-Mar-2023	12-Oct-2024	31-Mar-2023																																					
Tailings Storage Facility (TSF)																																										
A1190	Additional vegetation clearing of TSF	1.1y	31-Mar-2023	30-Apr-2024	31-Mar-2023																																					
A1200	Construction of the diversion works including the Davidson Creek Diversion System and Mine Area Creek Diversion	0.6y	15-Jun-2023	15-Jan-2024																																						
A1210	SCP and the associated inlet channels	0.9y	15-Jun-2023	30-Apr-2024																																						
A1220	Main Dam C – Excavation of cut-off-trench (COT) and initial fill placement	0.6y	03-Nov-2023	15-Jun-2024																																						
A1230	Main Dam C Stage 1 construction to 1,263 masl	0.9y	28-Dec-2023	01-Dec-2024																																						
A1240	TSF C Pond – Starter pond initiation at the Diversion Berm; Receipt of water from drainage area	0.8y	21-Jul-2023	30-Apr-2024																																						
A1250	Disposal of PAG & ML waste rock from open pit in designated disposal area located between Diversion Berm & Main Dam C	0.9y	28-Dec-2023	01-Dec-2024																																						
A1260	Water reclaim pipeline and reclaim pump systems from TSF C Pond – Siting and construction to pre-commissioning	0.9y	15-Jan-2024	17-Dec-2024																																						
A1270	Tailings distribution pipeline constructed -processing facility to the west side TSF C – Siting and const. to pre-comm	0.9y	15-Jan-2024	21-Nov-2024																																						
A1280	Construction of the IECD, pond and pumpback system	0.5y	08-Aug-2024	01-Feb-2025																																						
Waste Stockpiles (WSF)																																										
A1290	Vegetation clearing, grubbing, and surface preparation as required	0.1y	03-Jul-2025	23-Jul-2025																																						
A1300	Construction of Lower WSF water mgmt systems, including water collection channels & the Lower WSF Collection Pond	0.2y	23-Jul-2025	01-Oct-2025																																						
A1310	Lower Waste Stockpile – Development of lift to 1,420 masl	0.2y	23-Jul-2025	01-Oct-2025																																						
Low Grade Ore (LGO) Stockpile																																										
A1320	Vegetation clearing, grubbing, and surface preparation as required	0.8y	01-May-2024	30-Jan-2025																																						
A1330	Construction of water mgmt systems, including non-contact water diversions, contact water collection channels	0.5y	20-Aug-2024	15-Feb-2025																																						
A1340	Construction of water mgmt systems LGO Collection Pond, stockpile sub-grade preparation, and associated liner systems	0.5y	10-Oct-2024	08-Apr-2025																																						

Activity Duration
 Activity Duration
 summary

TASK filter: WBS .

Date	Revision	Checked	Approved
17-Jan-2025	V.7: Prepared pursuant to: Blackwater Decision Statement condition 11.2	BW	JNL / RT

Activity ID	Activity Name	Duration	Start	Finish	2023												2024												2025												026
					N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	O	
Water Management Structures																																									
A1370	Vegetation clearing, grubbing, and surface preparation as required	0.9y	31-Mar-2023	29-Feb-2024																																					
A1380	WMP construction, including berm construction, liner placement to form the pond, pond filling	0.9y	02-Jul-2023	12-May-2024																																					
A1390	Construction of associated water supply and discharge pump systems and pipelines	0.9y	29-Dec-2023	17-Nov-2024																																					
A1400	Open Pit dewatering activities, const & ops of dewatering & depressurization with discharge to Metals WPT, WMP or Plant	0.4y	12-Oct-2024	16-Mar-2025																																					
A1410	Central Diversion System construction, diversion channels, collection channels, water transfer pond, pumps/piping	1.2y	01-Dec-2023	25-Jan-2025																																					
A1420	FWR construction, commissioning, and operation	0.2y	24-Jul-2025	01-Oct-2025																																					
A1430	Surface drainage for infrastructure – construction and operation	2.5y	30-Apr-2023	01-Oct-2025																																					
Waste Treatment																																									
A1440	Construction of the Metals WTP	0.4y	03-May-2024	10-Sep-2024																																					
A1460	Construction of the lime neutralization system	0.8y	21-Mar-2024	09-Jan-2025																																					
Topsoil Stockpiles																																									
A1470	Vegetation clearing, grubbing, site leveling, stockpiling, and maintenance of salvaged soils	1.9y	31-Mar-2023	30-Jan-2025																																					
Mine Services and Haul Roads																																									
A1480	Mine Service Roads – Completion of service road network; Operations and maintenance	1.4y	01-Apr-2023	30-Aug-2024																																					
A1490	Ex-pit Haul Roads – Upgrading width and foundation; Construction and maintenance of pit access	1.5y	31-Jul-2023	21-Jan-2025																																					
A1500	In-pit Haul Roads – Construction and maintenance within operational pits	1.1y	07-Jan-2024	21-Jan-2025																																					
Power Supply and Distribution																																									
A1510	Vegetation clearing, grubbing, and surface preparation as required	0.3y	04-Dec-2023	31-Mar-2024																																					
A1520	Power to worksites provided by the portable gensets	1.7y	31-Mar-2023	15-Dec-2024																																					
A1530	Main substation and emergency power system developed to pre-commissioning	0.7y	13-Jan-2024	08-Oct-2024																																					
A1540	Connection of the mine site by the 230 kV transmission line	0.5y	01-Apr-2024	08-Oct-2024																																					
Explosives Storage Facility																																									
A1550	Complete vegetation clearing, grubbing and surface preparation as required	1.0y	20-Apr-2023	17-Apr-2024																																					
A1560	Construction, commissioning, and operation	0.5y	17-Apr-2024	31-Oct-2024																																					
Ancillary Structures																																									
A1570	Complete vegetation clearing, grubbing, and surface preparation as required	0.8y	31-Mar-2023	31-Dec-2023																																					
A1580	Construction laydown areas – Construction, commissioning, and operation	1.3y	10-Apr-2023	02-Aug-2024																																					

 Activity Duration
 Activity Duration
 summary

TASK filter: WBS .


































Date	Revision	Checked	Approved
17-Jan-2025	V.7: Prepared pursuant to:	BW	JNL / RT
	Blackwater Decision Statement condition 11.2		

Activity ID	Activity Name	Duration	Start	Finish	2024		2025				2026				2027				2028				2029				2030				2031				
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1		
Blackwater Gold Project					5.6y	02-Sep-2024	06-Mar-2030	[Summary bar]																											
3 - Year +1 to Year +5					5.6y	02-Sep-2024	06-Mar-2030	[Summary bar]																											
Open Pit					5.0y	01-Apr-2025	06-Mar-2030	[Summary bar]																											
A1730	Continued clearing of pit area	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025	[Activity bar]																													
A1740	Extraction Method - Diesel drill, blast and shovel; Addition of electric drill and shovel (Year +5)	1.0y	11-Mar-2029	06-Mar-2030		[Activity bar]																													
A1750	Installation of 4.16 kV substation to power electric drill and shovel (Year +5)	1.0y	11-Mar-2029	06-Mar-2030		[Activity bar]																													
A1760	Staged increase to in-pit mine fleet (Year +1)	1.0y	01-Apr-2025	27-Mar-2026	01-Apr-2025	[Activity bar]																													
A1762	Staged increase to in-pit mine fleet (Year +4)	1.0y	16-Mar-2028	11-Mar-2029		[Activity bar]																													
A1764	Staged increase to in-pit mine fleet (Year +5)	1.0y	11-Mar-2029	06-Mar-2030		[Activity bar]																													
A1770	Construction Borrow Pit – Mining to pit bottom 1,450 masl (Year +2)	1.0y	27-Mar-2026	22-Mar-2027		[Activity bar]																													
A1780	Starter Pit – Mining to pit bottom 1,450 masl (Year +3)	1.0y	22-Mar-2027	16-Mar-2028		[Activity bar]																													
A1790	East Pushback 1 – Mining to pit bottom 1,460 masl (Year +4)	1.0y	16-Mar-2028	11-Mar-2029		[Activity bar]																													
A1800	East Pushback 2 – Mining to 1,460 masl bench (Year +5)	1.0y	11-Mar-2029	06-Mar-2030		[Activity bar]																													
A1810	West Pushback – Mining to 1,540 masl bench (Year +5)	1.0y	11-Mar-2029	06-Mar-2030		[Activity bar]																													
Process Facilities					5.0y	01-Apr-2025	06-Mar-2030	[Summary bar]																											
A1820	Phase 1 commissioning and operations to 4.5 Mt per annum (Year +1) and 5.5 Mt per annum (Year +2)	2.0y	01-Apr-2025	22-Mar-2027	01-Apr-2025	[Activity bar]																													
A1830	Conduct upgrades to increase throughput to 12 Mt per annum (Year +5)	3.0y	22-Mar-2027	06-Mar-2030		[Activity bar]																													
Tailings Storage Facility (TSF)					5.6y	02-Sep-2024	06-Mar-2030	[Summary bar]																											
A1840	Main Dam C – Monitoring and annual raises up to 1,312 masl (Year +5)	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025	[Activity bar]																													
A1850	TSF C Pond – Receipt of discharge from mine site drainage network, IECD pond, and final ECD pond	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025	[Activity bar]																													
A1860	Additional receipt of discharge from water accumulated behind Main Dam D initial fill areas;	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025	[Activity bar]																													
A1870	With Impoundment of PAG and ML waste rock and tailings Serves as process water source	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025	[Activity bar]																													
A1880	Main Dam D – Initial construction of Stage 1 to 1,256 masl (Year +5)	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025	[Activity bar]																													
A1890	Water reclaim pump systems in the TSF C Pond used to reclaim water to the mill to support ore processing	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025	[Activity bar]																													
A1900	Expansion of water reclaim systems coinciding with processing facility expansions - Siting, Const & comm (Year +5)	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025	[Activity bar]																													
A1910	PAG/NAG3 waste rock disposal occurs within TSF C adjacent to Main Dam C	5.5y	03-Oct-2024	06-Mar-2030	Oct-2024	[Activity bar]																													
A1920	Tailing distribution systems and pipeline convey tailings to discharge location at west side of TSF C	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025	[Activity bar]																													
A1930	IECD and pond – Operational with pumpback to the TSF C Pond	5.6y	02-Sep-2024	05-Mar-2030	ep-2024	[Activity bar]																													
Waste Stockpiles (WSF)					5.0y	01-Apr-2025	06-Mar-2030	[Summary bar]																											
A1940	Vegetation clearing, grubbing, and surface preparation as required	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025	[Activity bar]																													
A1950	Lower Waste Stockpile – Stockpiling to 1,450 masl (Year +5)	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025	[Activity bar]																													

Activity Duration
 Activity Duration
 summary

TASK filter: Year 1 to 5.

Date	Revision	Checked	Approved
17-Jan-2025	V.7: Prepared pursuant to:	BW	JNL / RT
	Blackwater Decision Statement condition 11.2		




Activity ID	Activity Name	Duration	Start	Finish	2024		2025				2026				2027				2028				2029				2030				2031				
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1		
Low Grade Ore (LGO) Stockpiles					5.0y	01-Apr-2025	06-Mar-2030																												
A1960	Vegetation clearing, grubbing, and surface preparation as required	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025																														
A1970	Stockpiling of LGO Stockpile (lower grade ore) to lift height 1,500 masl (Year +3)	1.0y	22-Mar-2027	16-Mar-2028																															
A1980	Stockpiling of LGO Stockpile Pile A (higher grade ore) to lift height 1,470 masl (Year +3)	1.0y	22-Mar-2027	16-Mar-2028																															
Water Management Structures					5.0y	01-Apr-2025	06-Mar-2030																												
A1990	Open Pit dewatering	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025																														
A2000	WMP outflows pumped to Processing Plant and FWR	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025																														
Water Treatment					5.0y	08-Apr-2025	06-Mar-2030																												
A2010	Neutralization of Low Grade Ore (LGO) Stockpile runoff with lime before discharging to the TSF C Pond along with tailing	5.0y	08-Apr-2025	06-Mar-2030	08-Apr-2025																														
A2020	Treatment of water collecting in Open Pit & runoff from Lower Waste Stockpile treated by Metals WTP, if not going Plant	5.0y	08-Apr-2025	06-Mar-2030	08-Apr-2025																														
A2030	Treated water is used at the mill and excess treated water conveyed to WMP	5.0y	08-Apr-2025	06-Mar-2030	08-Apr-2025																														
A2040	Excess TSF C Pond water treatment at Membrane WTP and discharge to the WMP	3.7y	15-Jul-2026	06-Mar-2030																															
Mine Service and Haul Roads					5.0y	01-Apr-2025	06-Mar-2030																												
A2050	Ex-pit haul roads – Expansion to service development of the pit	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025																														
A2060	In-pit haul roads – Expansion to service development of the pit	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025																														
Mine Access Road (MAR)					4.7y	01-Jul-2025	06-Mar-2030																												
A1110	Tree clearing, bulk excavation and grading, surfacing and installation of bridges	4.7y	01-Jul-2025	06-Mar-2030	01-Jul-2025																														
Ready Line and Bulk Fuel Supply					1.0y	16-Mar-2028	11-Mar-2029																												
A2070	Fuel storage expanded to 300,000 L (Year +4)	1.0y	16-Mar-2028	11-Mar-2029																															
Ongoing Use and Maintenance					5.0y	01-Apr-2025	06-Mar-2030																												
A2080	Topsoil stockpiles	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025																														
A2090	Central Diversion System, WMP, and FWR	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025																														
A2100	Surface drainage for infrastructure	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025																														
A2110	Mine service roads	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025																														
A2120	Power supply and distribution	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025																														
A2130	Explosives storage facility	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025																														
A2140	Ancillary facilities	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025																														
A2150	Borrow pits and aggregate and concrete batch plants (Plant expansion)	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025																														
Off-Site Infrastructure					5.0y	01-Apr-2025	06-Mar-2030																												
A1690	Decommissioning of Exploration Access Road	1.0y	10-Jan-2029	05-Jan-2030																															
A2160	Transmission line	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025																														
A2170	Airstrip and airstrip access road – Construction and connection to Mine Access Road (MAR)	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025																														
A4120	Installation of Freshwater Supply System and Pumping and Pipeline systems from Tatelkuz Lake	5.0y	01-Apr-2025	06-Mar-2030	01-Apr-2025																														

 Activity Duration
 Activity Duration
 summary

TASK filter: Year 1 to 5.

Date	Revision	Checked	Approved
17-Jan-2025	V.7: Prepared pursuant to:	BW	JNL / RT
	Blackwater Decision Statement condition 11.2		

Activity ID	Activity Name	Duration	Start	Finish	2029		2030				2031				2032				2033				2034				2035				2036
					Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Blackwater Gold Project																															
4 - Year +6 to Year +10																															
Open Pit																															
A2180	Continued clearing of pit to final pit limits	5.0y	06-Mar-2030	08-Feb-2035	06-Mar-2030																										
A2190	Extraction Method – Diesel drill and shovel; Addition of a second electric drill and shovel (Year +9)	1.0y	18-Feb-2033	13-Feb-2034							18-Feb-2033					13-Feb-2034															
A2200	Installation of second 4.16 kV substation to power electric drill and shovel (Year +9)	1.0y	18-Feb-2033	13-Feb-2034							18-Feb-2033					13-Feb-2034															
A2210	Staged increase to in-pit mine fleet (Year +6)	1.0y	06-Mar-2030	01-Mar-2031	06-Mar-2030						01-Mar-2031																				
A2212	Staged increase to in-pit mine fleet (Year +8)	1.0y	24-Feb-2032	18-Feb-2033							24-Feb-2032					18-Feb-2033															
A2214	Staged increase to in-pit mine fleet (Year +10)	1.0y	13-Feb-2034	08-Feb-2035												13-Feb-2034															
A2220	East Pushback 2 – Mining to pit bottom 1,380 masl bench (Year +7)	1.0y	01-Mar-2031	24-Feb-2032		01-Mar-2031										24-Feb-2032															
A2230	West Pushback – Mining to pit bottom 1,300 masl bench (Year +9)	1.0y	18-Feb-2033	13-Feb-2034							18-Feb-2033										13-Feb-2034										
A2240	North Pushback 1 – Mining to 1,310 masl bench (Year +10)	1.0y	13-Feb-2034	08-Feb-2035												13-Feb-2034															
A2250	North Pushback 2 – Mining to 1,410 masl bench (Year +10)	1.0y	13-Feb-2034	08-Feb-2035												13-Feb-2034															
A2260	South Pushback – Mining to 1,670 masl bench (Year +10)	1.0y	13-Feb-2034	08-Feb-2035												13-Feb-2034															
Processing Plant																															
A2270	Phase 2 plan commissioning and operations to 12 Mtpa (Year +6)	1.0y	06-Mar-2030	01-Mar-2031	06-Mar-2030						01-Mar-2031																				
A2280	Initiate upgrades to increase annual throughput to 20 Mtpa (Year +10)	1.0y	13-Feb-2034	08-Feb-2035												13-Feb-2034															
Tailings Storage Facility (TSF)																															
A2290	West Dam – First stage lift construction to 1,345 masl including seepage monitoring sump and pumpback system (Year +6)	1.0y	06-Mar-2030	01-Mar-2031	06-Mar-2030						01-Mar-2031																				
A2300	Main Dam C – Monitoring and raises to 1,329 masl (Year +10)	1.0y	13-Feb-2034	08-Feb-2035												13-Feb-2034															
A2310	TSF C Pond – Receipt of discharge from mine site drainage network, flows pumped from TSF D	5.0y	06-Mar-2030	08-Feb-2035	06-Mar-2030																										
A2320	Receipt of neutralized low-grade ore stockpile runoff; impoundment of PAG and ML waste rock ends during Year +6;	1.0y	06-Mar-2030	01-Mar-2031	06-Mar-2030						01-Mar-2031																				
A2330	Continued impoundment of tailings; Serves as process water source	5.0y	06-Mar-2030	08-Feb-2035	06-Mar-2030																										
A2340	Main Dam D – Monitoring and annual raises to 1,298 masl (Year +10)	1.0y	13-Feb-2034	08-Feb-2035												13-Feb-2034															
A2350	TSF D Pond – Starting Year +7 may also receive discharge from mine site drainage network, ECD pond;	4.0y	01-Mar-2031	08-Feb-2035		01-Mar-2031															08-Feb-2035										
A2360	TSF D Pond discharge serves as process water source; Impoundment of PAG and ML waste rock beginning in Year +6	1.0y	06-Mar-2030	01-Mar-2031	06-Mar-2030						01-Mar-2031																				
A2370	Expansion of tailings distribution infrastructure in Year +6	1.0y	06-Mar-2030	01-Mar-2031	06-Mar-2030						01-Mar-2031																				
A2380	Addition of a secondary line to the southwest end of TSF C to West Dam, operational in approximately Year +6	1.0y	06-Mar-2030	01-Mar-2031	06-Mar-2030						01-Mar-2031																				
A2390	Installation of two pipelines to convey tailings along the crest of Main Dam C to discharge into TSF C beginning Year +7	1.0y	01-Mar-2031	24-Feb-2032		01-Mar-2031										24-Feb-2032															
A2400	Additional pipelines to cover PAG/NAG3 disposal area - siting and construction to pre-commissioning	1.0y	01-Mar-2031	24-Feb-2032		01-Mar-2031										24-Feb-2032															

 Activity Duration
 Activity Duration
 summary

TASK filter: Year 6 to 10.

Date	Revision	Checked	Approved
17-Jan-2025	V.7: Prepared pursuant to:	BW	JNL / RT
	Blackwater Decision Statement condition 11.2		



Table with columns for Activity ID, Activity Name, Duration, Start, Finish, and quarterly breakdowns for years 2029-2036. Includes summary rows for Waste Stockpiles (WSF), Low Grade Ore (LGO) Stockpile, Water Management Structures, Mine Service and Haul Roads, Power Supply and Distribution, Ready Line and Bulk Fuel Supply, and Water Treatment.

Activity Duration
Activity Duration
summary

TASK filter: Year 6 to 10.

Table with columns: Date, Revision, Checked, Approved. Contains revision details and approval signatures.



Activity ID	Activity Name	Duration	Start	Finish	2029		2030				2031				2032				2033				2034				2035				2036			
					Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1		
A2600	Excess TSF C Pond water treatment at Membrane WTP and discharge to the WMP	5.0y	06-Mar-2030	08-Feb-2035	06-Mar-2030	[Green bar]																												08-Feb-2035
Ongoing Use and Maintenance		5.0y	06-Mar-2030	08-Feb-2035	[Black arrow summary]																													
A2610	Topsoil stockpiles erosion control and invasive plant management	5.0y	06-Mar-2030	08-Feb-2035	06-Mar-2030	[Green bar]																												08-Feb-2035
A2620	Central and Northern Diversion systems and Central Water Transfer Pond North and South Interception trenches	5.0y	06-Mar-2030	08-Feb-2035	06-Mar-2030	[Green bar]																												08-Feb-2035
A2630	Pit dewatering	5.0y	06-Mar-2030	08-Feb-2035	06-Mar-2030	[Green bar]																												08-Feb-2035
A2640	Fresh Water Reservoir (FWR)	5.0y	06-Mar-2030	08-Feb-2035	06-Mar-2030	[Green bar]																												08-Feb-2035
A2650	Surface drainage for Infrastructure	5.0y	06-Mar-2030	08-Feb-2035	06-Mar-2030	[Green bar]																												08-Feb-2035
A2660	Mine service roads	5.0y	06-Mar-2030	08-Feb-2035	06-Mar-2030	[Green bar]																												08-Feb-2035
A2670	Ex-pit haul roads	5.0y	06-Mar-2030	08-Feb-2035	06-Mar-2030	[Green bar]																												08-Feb-2035
A2680	Power supply and distribution to other mine site components	5.0y	06-Mar-2030	08-Feb-2035	06-Mar-2030	[Green bar]																												08-Feb-2035
A2690	Explosives storage facility	5.0y	06-Mar-2030	08-Feb-2035	06-Mar-2030	[Green bar]																												08-Feb-2035
A2700	Ancillary structures	5.0y	06-Mar-2030	08-Feb-2035	06-Mar-2030	[Green bar]																												08-Feb-2035
A2710	Borrow pits and aggregate and concrete batch plant (Plant expansion)	5.0y	06-Mar-2030	08-Feb-2035	06-Mar-2030	[Green bar]																												08-Feb-2035
Off-Site Infrastructure		5.0y	06-Mar-2030	08-Feb-2035	[Black arrow summary]																													
A2720	Transmission line	5.0y	06-Mar-2030	08-Feb-2035	06-Mar-2030	[Green bar]																												08-Feb-2035
A2730	Freshwater supply system (FWSS) intake, pump stations and pipeline	5.0y	06-Mar-2030	08-Feb-2035	06-Mar-2030	[Green bar]																												08-Feb-2035
A2740	Airstrip and airstrip access road	5.0y	06-Mar-2030	08-Feb-2035	06-Mar-2030	[Green bar]																												08-Feb-2035

[Green bar] Activity Duration
[Green bar] Activity Duration
[Black arrow] summary

TASK filter: Year 6 to 10.

Date	Revision	Checked	Approved
17-Jan-2025	V.7: Prepared pursuant to: Blackwater Decision Statement condition 11.2	BW	JNL / RT

Activity ID	Activity Name	Duration	Start	Finish	2033	2034	2035	2036	2037	2038	2039	2040	2041	2042	2043	2044	2045	2046	2047								
					Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q				
Blackwater Gold Project																											
5 - Year +11 to Year +18																											
Open Pit																											
A2750	Extraction Method – Diesel drill and shovel, and electric drill and shovel	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035																						
A2760	Staged decrease to in-pit mine fleet (Year +15, Year +16, Year +17, Year +18)	4.0y	18-Jan-2039	28-Dec-2042					18-Jan-2039																		
A2770	North Pushback 1 – Mining to pit bottom 1,260 masl bench (Year +11)	1.0y	08-Feb-2035	03-Feb-2036	08-Feb-2035																						
A2780	North Pushback 2 – Mining to pit bottom 1,140 masl bench (Year +14)	1.0y	23-Jan-2038	18-Jan-2039				23-Jan-2038																			
A2790	South Pushback – Mining to pit bottom 1,160 masl bench (Year +18)	1.0y	02-Jan-2042	28-Dec-2042								02-Jan-2042															
Processing Plant																											
A2800	Phase 3 of plant commissioning and operations to 20 Mtpa (Year +11)	1.0y	08-Feb-2035	03-Feb-2036	08-Feb-2035																						
Tailings Storage Facility (TSF)																											
A2810	Main Dam C – Monitoring and annual raises to final elevation of 1,353 masl (Year +18)	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035																						
A2820	West Dam – Monitoring and raised to final elevation of 1,353 masl (Year +12)	1.0y	03-Feb-2036	28-Jan-2037		03-Feb-2036																					
A2830	Saddle Dam – Initial const to 1,337 masl (Year +12) raise in two stages to final elev of 1,353 masl by Year +18)	7.0y	03-Feb-2036	28-Dec-2042		03-Feb-2036																					
A2840	TSF C Pond – Receipt of mine site drainage & Open Pit; Impoundment of tailings ends in approx Year +21	11.0y	08-Feb-2035	12-Dec-2045	08-Feb-2035															12-Dec-2045							
A2850	TSF C Pond – Serves as process water source.	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035																						
A2860	Main Dam D – Monitoring and annual raises to the ultimate build of 1,324 masl (Year +18)	7.5y	08-Feb-2035	01-Jul-2042	08-Feb-2035																						
A2870	TSF D Pond - Receipt of mine site drainage network, ECD Pond, & Open Pit until Year +19	9.0y	08-Feb-2035	23-Dec-2043	08-Feb-2035															23-Dec-2043							
A2880	TSF D Pond - Impoundment of PAG; Serves as process water source	9.0y	08-Feb-2035	23-Dec-2043	08-Feb-2035																23-Dec-2043						
A2890	ECD and Pond– Monitoring of dam and pond; Pumpback of water to the TSF D Pond	11.0y	08-Feb-2035	12-Dec-2045	08-Feb-2035															12-Dec-2045							
Waste Stockpiles (WSF)																											
A2900	Lower Waste Stockpile – Resloping, geotechnical stabilization, and monitoring	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035																						
A2910	Upper Waste Stockpile – Expansion to 1,620 masl lift with cessation of stockpiling (Year +18)	1.0y	02-Jan-2042	28-Dec-2042								02-Jan-2042															
Low Grade Ore (LGO) Stockpile																											
A2920	Vegetation clearing, grubbing, and surface preparation as required	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035																						
A2930	Stockpiling of LGO Stockpile to lift height 1,540 masl (Year +13)	1.0y	28-Jan-2037	23-Jan-2038			28-Jan-2037																				
A2932	Stockpiling of LGO Stockpile to lift height 1,520 masl (Year +18)	1.0y	02-Jan-2042	28-Dec-2042								02-Jan-2042															
A2940	Stockpiling of LGO Stockpile Pile A to lift height 1,480 masl (Year +13)	1.0y	28-Jan-2037	23-Jan-2038			28-Jan-2037																				

 Activity Duration
 Activity Duration
 summary

TASK filter: Year 11 to 18.

Date	Revision	Checked	Approved
17-Jan-2025	V.7: Prepared pursuant to:	BW	JNL / RT
	Blackwater Decision Statement condition 11.2		



Activity ID	Activity Name	Duration	Start	Finish	2033	2034	2035	2036	2037	2038	2039	2040	2041	2042	2043	2044	2045	2046	2047	
					Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
A2942	Stockpiling of LGO Stockpile Pile A height 1,480 masl, handling to commence in Year +15,	1.0y	18-Jan-2039	13-Jan-2040						18-Jan-2039		13-Jan-2040								
A2950	Low Grade Ore (LGO) Stockpile Pile A will be depleted by Year +18	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
Water Treatment		8.0y	08-Feb-2035	28-Dec-2042	[Green bar]															
A2960	Neutralization of Low Grade Ore (LGO) Stockpile runoff with lime before discharge along with tailings to TSF C	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
A2970	Treatment of waters from the Open Pit and runoff from the Upper and Lower Waste Stockpiles treated by Metals WTP	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
A2980	Metals WTP treated water is used at the mill and excess treated water conveyed to WMP	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
A2990	Excess TSF C Pond water treatment at Membrane WTP and discharge to the WMP, if req'd due to prevailing climate condition	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
Water Management Structures		1.0y	03-Feb-2036	28-Jan-2037	[Green bar]															
A3000	Water Management Pond relocated to accommodate continued filling of TSF C (Year +12)	1.0y	03-Feb-2036	28-Jan-2037			03-Feb-2036													
Mine Service and Haul Roads		8.0y	08-Feb-2035	28-Dec-2042	[Green bar]															
A3010	In-pit haul roads – Expansion to service pit expansion	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
Components Ongoing Use and Maintenance		8.0y	08-Feb-2035	28-Dec-2042	[Green bar]															
A3020	Topsoil stockpiles	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
A3030	Central and Northern Diversion Systems	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
A3040	ECD, interception trenches, and pumpback system	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
A3050	FWR	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
A3060	Surface drainage for infrastructure	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
A3070	Mine service roads	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
A3080	Ex-pit haul roads	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
A3090	Power supply and distribution	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
A3100	Explosives storage facility	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
A3110	Ancillary facilities	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
A3120	Borrow pits and aggregate sources	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
Off-Site Infrastructure		8.0y	08-Feb-2035	28-Dec-2042	[Green bar]															
A3130	Transmission line	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
A3140	FWSS pumphouse and pipeline	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				
A3150	Airstrip and airstrip access road	8.0y	08-Feb-2035	28-Dec-2042	08-Feb-2035	[Green bar]										28-Dec-2042				

[Green bar] Activity Duration
 [Green bar] Activity Duration
 [Arrow] summary

TASK filter: Year 11 to 18.

Date	Revision	Checked	Approved
17-Jan-2025	V.7: Prepared pursuant to:	BW	JNL / RT
	Blackwater Decision Statement condition 11.2		



Activity ID	Activity Name	Duration	Start	Finish	2042				2043				2044				2045				2046				2047				2048		
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
Blackwater Gold Project																															
6 - Year +19 to Year +23																															
Open Pit																															
A3160	Decommissioning of mine fleet and electrical distribution system, de-watering wells, sumps, and related works	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																										
A3170	Initiate filling of Pit Lake (See Water Management Structures)	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																										
Processing Plant																															
A3180	Milling of Low Grade Ore (LGO) Stockpile reclaim at 20 Mt per annum (Year +19 to Year +22)3	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																										
Tailings Storage Facility (TSF)																															
A3190	West Dam – Monitoring and maintenance	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																										
A3200	Main Dam C – Monitoring and maintenance of dam	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																										
A3210	TSF C Pond – Conveyance of supernatant to Open Pit starting Year +19; Serves as process water source;	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																										
A3220	TSF C Pond – tailings infill ceases Year +21	3.0y	28-Dec-2042	12-Dec-2045	28-Dec-2042																										
A3230	Main Dam D – Monitoring and maintenance and raised to final elevation of 1,331 masl (Year +20)	1.0y	23-Dec-2043	17-Dec-2044																											
A3240	TSF D Pond – Receipt from mine site drainage network; impoundment of PAG, impoundment of tailings starting in Year +21	3.0y	17-Dec-2044	02-Dec-2047																											
A3250	TSF D Pond – serves as process water source	3.0y	17-Dec-2044	02-Dec-2047																											
A3260	ECD and Pond – Monitoring of dam and pond; Conveyance of captured flows to Open Pit starting Year +19	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																										
Waste Stockpiles (WSF)																															
A3270	Lower Waste Stockpile – Resloping, geotechnical stabilization, and monitoring	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																										
A3280	Upper Waste Stockpile – Resloping, geotechnical stabilization, and monitoring	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																										
Low Grade Ore (LGO) Stockpile																															
A3290	Re-handling of ore to Processing Plant with depletion by Year +23	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																										
A3300	Closure and progressive reclamation	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																										
Water Management Structures																															
A3310	Pit Lake – Filling with natural groundwater and TSF C Pond supernatant (Year +20 to Year +23), and ECD Pond	4.0y	23-Dec-2043	02-Dec-2047																											
A3320	Lower Waste Stockpile runoff directed to TSF C Pond and Upper Waste Stockpile runoff directed to Open Pit	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																										
A3330	Continued operation of FWR for mill processing supply and Davidson Creek instream flow needs (IFN)	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																										
A3340	Continued operation of the Central and Northern Diversion Systems with water conveyed to the WMP and FWR, respectively	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																										
Water Treatment																															

Activity Duration
 Activity Duration
 summary

TASK filter: Year 19 to 23.

Date	Revision	Checked	Approved
17-Jan-2025	V.7: Prepared pursuant to: Blackwater Decision Statement condition 11.2	BW	JNL / RT



Activity ID	Activity Name	Duration	Start	Finish	2042				2043				2044				2045				2046				2047				2048		
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
A3350	Continued operation of the lime neutralization for Low Grade Ore (LGO) Stockpile runoff	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						
A3360	Metals treatment for pit dewatering, the Upper and Lower Waste Stockpiles not required.	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						
A3370	Pit water will be allowed to naturally flow into the Open Pit to aid in pit filling.	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						
A3380	Lower WSP water will be directed to the TSF; Upper WSP water will be directed to the Open Pit and TSF.	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						
A3390	Membrane treatment of excess TSF C water not required as it will be pumped to the Open Pit to aid in pit filling	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						
Mine Service and Haul Roads		5.0y	28-Dec-2042	02-Dec-2047																											
A3400	Ex-pit haul roads – Progressive closure and reclamation	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						
A3410	In-pit haul roads – Closure and progressive inundation of in-pit haul roads (Year +19)	1.0y	28-Dec-2042	23-Dec-2043	28-Dec-2042				23-Dec-2043																02-Dec-2047						
Power Supply and Distribution		5.0y	28-Dec-2042	02-Dec-2047																											
A3420	Decommissioning of electrical distribution to Open Pit for drills and shovels	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						
Explosives Storage Facility		5.0y	28-Dec-2042	02-Dec-2047																											
A3430	Progressive closure and reclamation	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						
Components Ongoing Use and Maintenance		5.0y	28-Dec-2042	02-Dec-2047																											
A3440	Topsoil stockpiles	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						
A3450	Central and Northern Diversion Systems	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						
A3460	ECD, interception trenches, and pumpback system	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						
A3470	FWR Surface drainage for infrastructure	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						
A3480	Mine service roads	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						
A3490	Power supply and distribution	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						
A3500	Ancillary facilities	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						
A3510	Borrow pits and aggregate sources	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						
Off-Site Infrastructure		5.0y	28-Dec-2042	02-Dec-2047																											
A3520	Transmission Line	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						
A3530	FWSS pumphouse and pipeline	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						
A3540	Airstrip and airstrip access road	5.0y	28-Dec-2042	02-Dec-2047	28-Dec-2042																				02-Dec-2047						

Activity Duration
 Activity Duration
 summary

TASK filter: Year 19 to 23.

Date	Revision	Checked	Approved
17-Jan-2025	V.7: Prepared pursuant to:	BW	JNL / RT
	Blackwater Decision Statement condition 11.2		






Activity ID	Activity Name	Duration	Start	Finish	2047				2048				2049				2050				2051				2052				2053				2054	
					Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1
Blackwater Gold Project					[Summary bar]																													
7 - Year +24 to Year +45					[Summary bar]																													
Open Pit					[Summary bar]																													
A3550	Filling of Pit Lake to be completed (Year +45)	22.0y	02-Dec-2047	08-Aug-2069	[Activity bar: 02-Dec-2047 to 08-Aug-2069]																													
Processing Plant					[Summary bar]																													
A3560	Decommissioning (Year +24 and Year +25)	2.0y	02-Dec-2047	21-Nov-2049	[Activity bar: 02-Dec-2047 to 21-Nov-2049]																													
A3562	Reclamation (Year +26 onwards)	20.0y	21-Nov-2049	08-Aug-2069	[Activity bar: 21-Nov-2049 to 08-Aug-2069]																													
Tailings Storage Facility (TSF)					[Summary bar]																													
A3570	Reclamation of dams/tailings beaches	22.0y	02-Dec-2047	08-Aug-2069	[Activity bar: 02-Dec-2047 to 08-Aug-2069]																													
Waste Stockpiles (WSF)					[Summary bar]																													
A3580	Lower Waste Stockpile – Rehandling material for reclamation purposes followed by reclamation and monitoring	22.0y	02-Dec-2047	08-Aug-2069	[Activity bar: 02-Dec-2047 to 08-Aug-2069]																													
A3590	Upper Waste Stockpile – Reclamation followed by monitoring	22.0y	02-Dec-2047	08-Aug-2069	[Activity bar: 02-Dec-2047 to 08-Aug-2069]																													
Low Grade Ore (LGO) Stockpile					[Summary bar]																													
A3600	Reclaimed with monitoring and maintenance as required	22.0y	02-Dec-2047	08-Aug-2069	[Activity bar: 02-Dec-2047 to 08-Aug-2069]																													
Topsoil Stockpiles					[Summary bar]																													
A3610	Handling and distribution of salvaged soil with eventual closure and reclamation of the stockpiles (Year +26)	1.0y	21-Nov-2049	16-Nov-2050	[Activity bar: 21-Nov-2049 to 16-Nov-2050]																													
Mine Service and Haul Roads					[Summary bar]																													
A3620	Operation and maintenance of roads needed for the Closure phase	22.0y	02-Dec-2047	08-Aug-2069	[Activity bar: 02-Dec-2047 to 08-Aug-2069]																													
A3630	Decommissioning and reclamation of other roads	22.0y	02-Dec-2047	08-Aug-2069	[Activity bar: 02-Dec-2047 to 08-Aug-2069]																													
Power Supply and Distribution					[Summary bar]																													
A3640	Operation and maintenance of power supply and distribution needed for the Closure phase	22.0y	02-Dec-2047	08-Aug-2069	[Activity bar: 02-Dec-2047 to 08-Aug-2069]																													
A3650	Decommissioning and reclamation of other components of the power supply	22.0y	02-Dec-2047	08-Aug-2069	[Activity bar: 02-Dec-2047 to 08-Aug-2069]																													
Ancillary Structures					[Summary bar]																													
A3660	Helipad – Decommissioning and reclamation (Year +25)	1.0y	21-Nov-2049	16-Nov-2050	[Activity bar: 21-Nov-2049 to 16-Nov-2050]																													
A3670	Camp Facilities – Decommissioning and reclamation (Year +26)	1.0y	16-Nov-2050	11-Nov-2051	[Activity bar: 16-Nov-2050 to 11-Nov-2051]																													
A3680	Construction Laydown Areas – Decommissioning and reclamation (Year +26)	1.0y	16-Nov-2050	11-Nov-2051	[Activity bar: 16-Nov-2050 to 11-Nov-2051]																													
A3690	Truck shop/Mine office – Modification for vehicle servicing, fuel storage and dispensing, for Closure Phases (Year +26)	1.0y	16-Nov-2050	11-Nov-2051	[Activity bar: 16-Nov-2050 to 11-Nov-2051]																													
A3700	Mine site shop, warehousing, offices and accommodations for Closure Phases (Year +26)	1.0y	16-Nov-2050	11-Nov-2051	[Activity bar: 16-Nov-2050 to 11-Nov-2051]																													
A3710	Ready Line and Bulk Fuel Storage area – Decommissioning and reclamation (Year +26)	1.0y	16-Nov-2050	11-Nov-2051	[Activity bar: 16-Nov-2050 to 11-Nov-2051]																													
A3720	Waste Management Facilities – Decommissioning and reclamation (Year +26)	1.0y	16-Nov-2050	11-Nov-2051	[Activity bar: 16-Nov-2050 to 11-Nov-2051]																													

Activity Duration
 Activity Duration
 summary

TASK filter: WBS .

Date	Revision	Checked	Approved
17-Jan-2025	V.7: Prepared pursuant to:	BW	JNL / RT
	Blackwater Decision Statement condition 11.2		

		2055				2056				2057				2058				2059				2060				2061				2062				2063				2064				2065				2066				2067				2068				2069				2070	
Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2												
																																												08-Aug-2069																			
																																												08-Aug-2069																			
																																												08-Aug-2069																			
																																												13-Aug-2068		08-Aug-2069																	

 Activity Duration
 Activity Duration
 summary

TASK filter: WBS .

Date	Revision	Checked	Approved
17-Jan-2025	V.7: Prepared pursuant to:	BW	JNL / RT
	Blackwater Decision Statement condition 11.2		

